

August 2023

PUBLIC WORKS MONTHLY REPORT



PROGRAMS

Sign Replacement Program


The Public Works Sign Department has been working in zone 2 replacing street ID's. Thus far, 150 street ID's have been changed over to the new design in zones 1 and 2. The old signs have been made available for purchase and all proceeds will be donated to the E Angels Program.



Mowing

The Public Works team members have been busy mowing the City's parks and right of ways. A crew of 4 team members are scheduled to cut all the parks and right of ways every week. PW crews have worked **511** man hours to keep our parks and right of ways looking exceptional. August has been relatively hot and dry. The Public Works Department has also been continuously watering the new installs at Cahill Commons and the new trees throughout the city.

MOWING MAN HOURS FOR AUGUST 5yr CYCLE

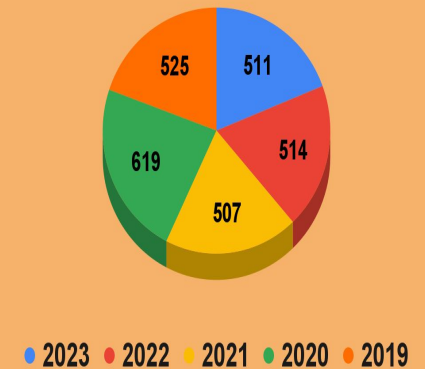

CAPITAL PROJECTS

New Public Works Facilities

Mark Spaulding Construction is currently working with Advantage Structural Engineers on footing and wall design for the Administration and Salt buildings. Permits have been submitted for the water service and sprinkler system as well. We are hopeful to see much more progress in September.

Concrete Street Reconstruction Projects

Eaton Asphalt is continuing on with the Jacqueline Dr., Kimberly Dr., Mitten Dr. and Debbie Ln. project which is approximately 90% complete. The concrete work on Jacqueline Dr. has been finished with a small section of street still remains to be milled and overlaid. The concrete work on Kimberly Dr. is complete with exception of a few sidewalk panels where Windstream needs to install a new box for Fiber Optic lines. The concrete work on Debbie Ln. is complete and 80% of concrete work on Mitten Dr. is complete. Once all the concrete work is complete, all the milling and new blacktop will be done at one time.

Upcoming Projects

The City accepted bids on July 12th for a street overlay project and a street reconstruction project. Riegler Blacktop was awarded the Crestside Court, Spire Circle and Summitridge Lane asphalt overlay project and Jefferson Contracting was awarded the Circlewood Drive concrete reconstruction project from Ridgewood Drive to Heartwood Lane.

Capital Park Improvements

Beaumont Building Group is awaiting an update on lead time for the playground equipment in order to leave Cahill Commons playset and basketball court in place as long as possible since phase I if this project had the park closed for most of the summer. Phase 2 of this project will be a nice change to what we have been accustomed to.

Railroad Underpass Painting Project

The Public Works Department has finally been assigned a Construction Manager through Norfolk Southern for the painting project and are anticipating a pre-construction meeting within the next couple of weeks. After this meeting we will have one more with the Bridge Supervisor and Flagmen then we should begin.


EXCEPTIONAL

EMPLOYEES • SERVICES • COMMUNITY




CODE ENFORCEMENT

- **\$2,300** total citation fees
- **\$900** voided citation fees

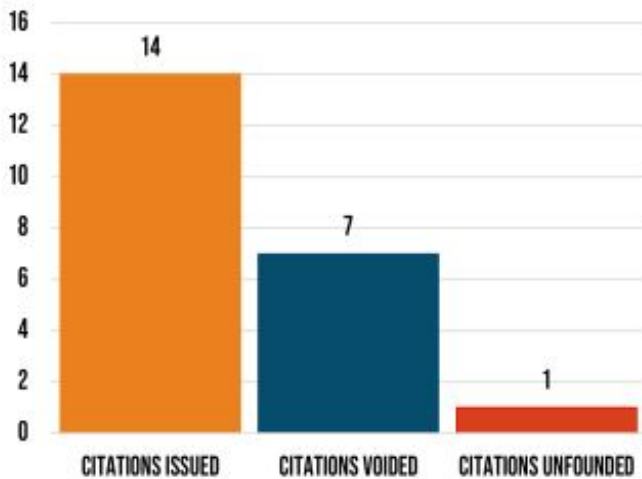


COMPLAINTS

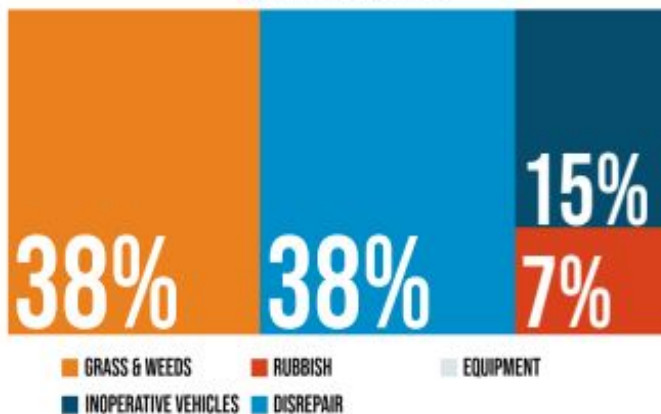

INSPECTIONS


- **80** total inspections

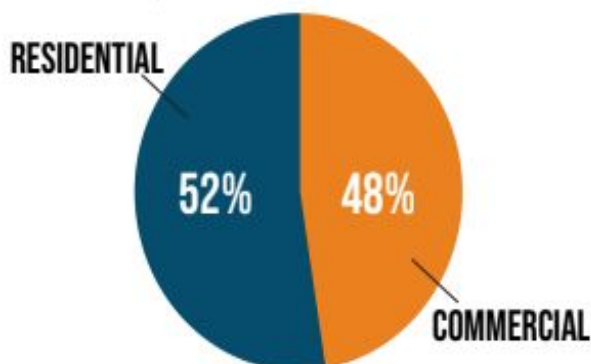


PERMITS

- **52** total permits
 - **22** building only permits
 - **5** zoning only permits
 - **10** building & zoning permits
 - **15** electric permits

BUILDING ONLY

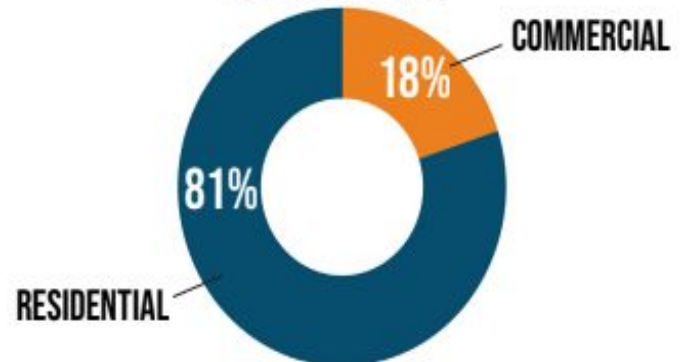

ZONING ONLY



BUILDING & ZONING

