## September 2024 PUBLIC WORKS MONTHLY REPORT



#### **PROGRAMS**

#### **Summer Send Off**

The PW team spent the month preparing for Summer Send Off and the Summer Send Off 5K. The countless hours that went into the planning and execution really shined at the event. The addition of the new shelters and concrete helped set this year apart.



#### **Cahill Commons**

The PW team also put the final touches on Cahill Commons for the dedication and unveiling of the sign. This included installing a dry stack wall with landscaping, lighting, and the sign itself. This entire project was completed in house at a huge cost savings.



#### **CAPITAL PROJECTS**

#### **New Public Works Facilities**

Work continues on all aspects of the new facility with the end in sight. All the LVT flooring, tile, cabinets, plumbing fixtures, light fixtures have been installed. Concrete works continues on the parking lot with just a few sections left to pour.

#### **Street Reconstruction Projects**

The first couple of street projects of the new fiscal year went out to bid, with the bids being opened in August. The first project will see full concrete street replacements on Hayden Place and Yager Court. The contract was awarded to Jefferson Contracting with a tentative start date of mid October. The Public Works Department will host a Public Workshop on October 3 at the Public Works Facility to let residents come and see what is taking place and to ask any guestions.

The second project will be an asphalt overlay on Theodore Place with the contract being awarded to Riegler Blacktop with a tentative start date of mid October.

#### **Annual Programs**

There are three programs that the Public Works Department puts out to bid annually and they are Sidewalk Replacement, Crack Sealing, and Street Striping.

#### Sidewalk Replacement Program

The sidewalk replacement contract was awarded to Humphrey Concrete. The plan is to start in early fall with completion before the winter months.

#### **Crack Sealing**

The crack sealing contract was award to Scodeller Construction. A start date in early spring is expected.

#### **Street Striping**

The street striping contract was awarded to A&A Safety and was completed in August.

#### **Capital Park Improvements**

John P. Tumlin and Sons have finished the construction side of Phase 3 at Silverlake Park with the installation of 2 shelters, new electric and a concrete plaza. They still need to put the tables, trash cans and grills in place when they arrive. Like everywhere else, there are supply shortages causing the delay.






## MONTHLY REPORT

September 2024


# CODE ENFORCEMENT CITATIONS

- \$11,700 total citation fees
- \$100 voided citation fees






### COMPLAINTS



## **PERMITS**

- 60 total permits
  - 3 building only permits
  - 6 zoning only permits
  - 18 building & zoning permits
  - 19 HVAC permits
  - 14 electric permits

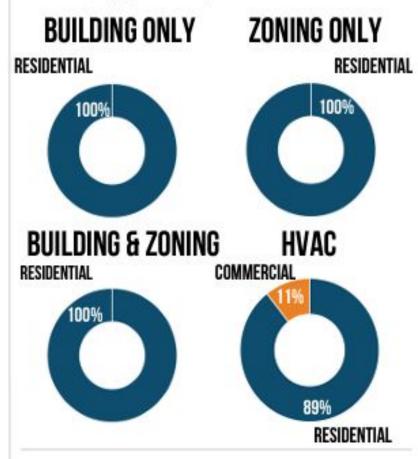

## INSPECTIONS

71 total inspections

