

November 2023

PUBLIC WORKS MONTHLY REPORT



PROGRAMS

Banners

The Honor Banners with the American Flags were taken down for the season and will be cleaned and stored until they go back up in early May, 2024. The **(48)** Holiday Banners along Dixie Highway and **(20)** New Charley Harper Art inspired banners on Commonwealth Avenue went up in their place to be displayed through the Holiday Season and will come down in early January, 2024

Playground Inspection

The City of Erlanger Public Works Department has **3** certified playground inspectors. In November of each year all **12** parks are thoroughly inspected to make sure the equipment is in good safe condition. If any problems are found, they are classified from non critical to critical. If a critical issue is found, that area of the playset or the whole playset will be closed down until repairs are made. Most items that are found are easily fixed at the time of the inspection. This year's inspections yielded a few small issues that have already been fixed. Team members spent **2** days with a total of **16** man hours to complete the inspections. The team members will follow up the inspection with a report that is kept on file at the Public Works Department.

Weather Warriors

The Public Works Department has begun setting up all of the large Dump Trucks for snow operations. All other equipment has been tested to make sure its operational and will be installed at the first indication of a weather event.



CAPITAL PROJECTS

New Public Works Facilities

McD Concrete has begun with footers and setting wall panels for the retaining walls along the rear of the maintenance building and dumpster drop down area. Water has been connected to the site as well. Footings and walls will continue as long as weather permits.

Concrete Street Reconstruction Project

Jefferson Contracting started the project on Circlewood Drive between Ridgewood Drive and Heartwood Lane on Monday November 6th. They have completed one side with exception of half of the intersection with Valleywood Ct, replacing the street as well as the sidewalks and aprons. They made sure to have it all wrapped up and that every resident had driveway access for the Thanksgiving Holiday. They continued the week after Thanksgiving starting on the other side and still plan on being wrapped up in the next few weeks.

Street Repaving Project

Eaton Asphalt has completed the project on Jacqueline Drive, Kimberly Drive, Mitten Drive, and Debbie Lane.

Capital Park Improvements

Beaumont Building Group continues with the Phase II renovation to Cahill Commons with the installation of the seat/retaining wall that separates the playground and basketball court. Work will continue as weather permits.

EXCEPTIONAL

EMPLOYEES • SERVICES • COMMUNITY



PDS


MONTHLY REPORT

November 2023

CODE ENFORCEMENT CITATIONS

• **\$4,700** total citation fees


• **\$500** voided citation fees

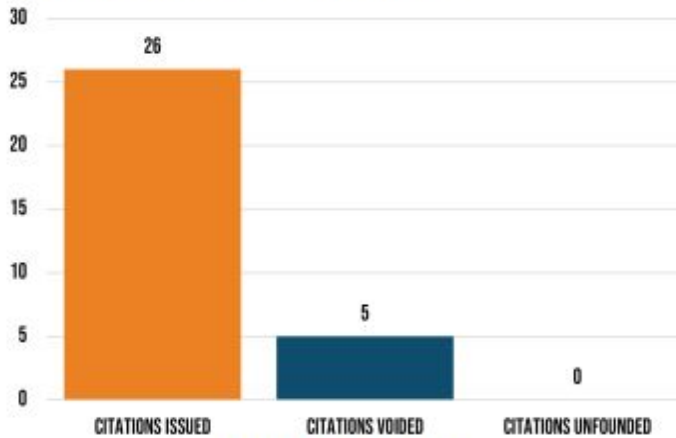

VIOLATIONS




COMPLAINTS

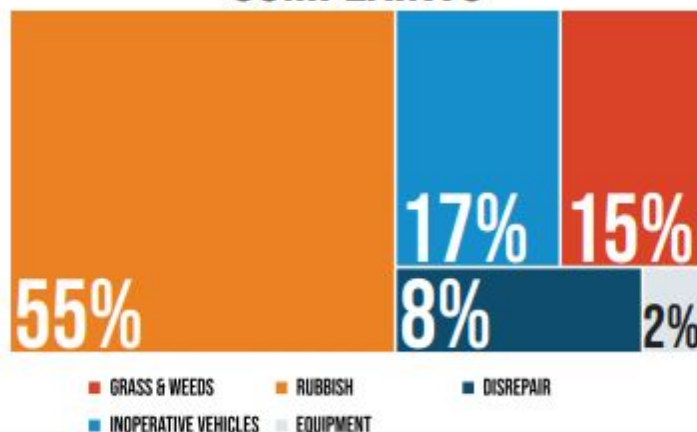


PERMITS

- **36** total permits
 - **2** building only permits
 - **3** zoning only permits
 - **6** building & zoning permits
 - **9** HVAC permits
 - **16** electric permits


BUILDING ONLY

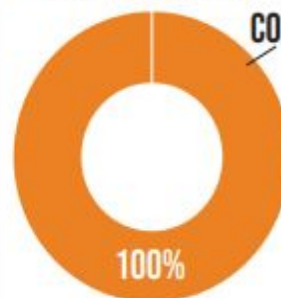


ZONING ONLY

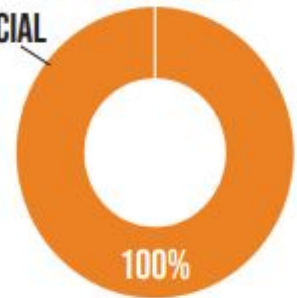

BUILDING & ZONING

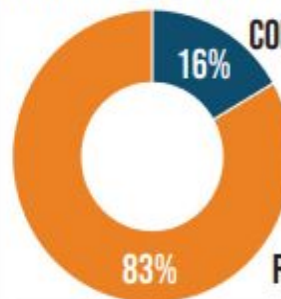

HVAC

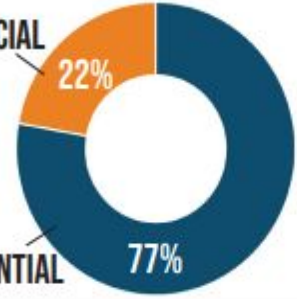

INSPECTIONS

- **67** total inspections

