

May 2025

PUBLIC WORKS MONTHLY REPORT



PROGRAMS

Mowing

The Public Works team members continue mowing the City's parks and right of ways. A crew of 4 team members are scheduled to cut all the parks and right of ways every week. PW crews have worked **400.5** man hours to keep our parks and streets looking exceptional.


Mulching

The PW's Department annually has all beds and tree rings mulched prior to Memorial Day. The department does a majority of the mulching in house and utilizes contractors to mulch six locations throughout the City. This year Maddox Landscaping received the bid for the contracted mulching. All mulching has been completed for this year.

Erlanger Salutes

The Erlanger Salutes Banner Program was created for the community to recognize and honor individuals on active duty, living, retired, and deceased service personnel by displaying the honoree's photo, name, rank, and armed service branch on a banner to be flown from utility poles throughout the City of Erlanger. All banners are displayed with an American flag. Banners will be displayed on Commonwealth Avenue, from Baker Street to Dixie Highway, and on Dixie Highway within Erlanger city limits. When this program started we had 13 honorees. This year, team members hung 97 banners.

MOWING MAN HOURS FOR MAY: 5 YEAR CYCLE

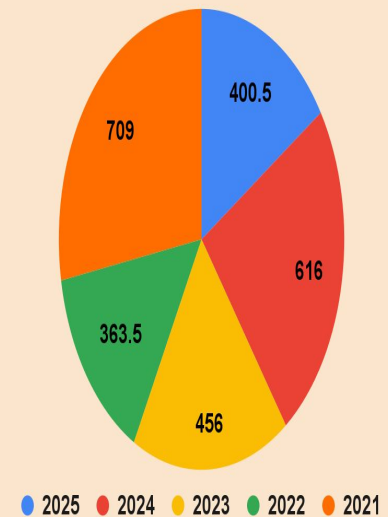

CAPITAL PROJECTS

Street Reconstruction Projects

Kentaboo Avenue and Virginia Avenue reconstruction project is about halfway completed. Both sides of Kentaboo Avenue and Virginia Avenue from the Florence line to the intersection has been replaced.

Hallam Avenue is close to completion. All the concrete work has been completed, the new layer of asphalt has been applied and all that is left is for the contractor to do yard restoration.

Elm Street is completed from Erlanger Road to Graves Avenue. The section from Graves Avenue to Bartlett Street is slated to get done the first part of June.

Yager Court is slated to start in Early June. It will get completely replaced with new sidewalks and driveway aprons.

The Narrows Road bridge replacement project is getting closer to completion. The new beams were delivered and set in place on Tuesday May, 27th with the decking and guardrail to follow.

Sherbourne Drive island project is close to completion. The project is slated to wrap up in early June.

Sidewalk Replacement Program

The sidewalk program for FY 24/25 is complete. This project will pick back up in FY 25/26

Park Project

Sherbourne Park is moving forward with the new shelter and new playground being installed and certified playground mulch is being put down around the playground.

EXCEPTIONAL

EMPLOYEES • SERVICES • COMMUNITY



PDS


MONTHLY REPORT

May 2025


CODE ENFORCEMENT

CITATIONS


- **\$13,600** total citation fees
- **\$100** voided citation fees

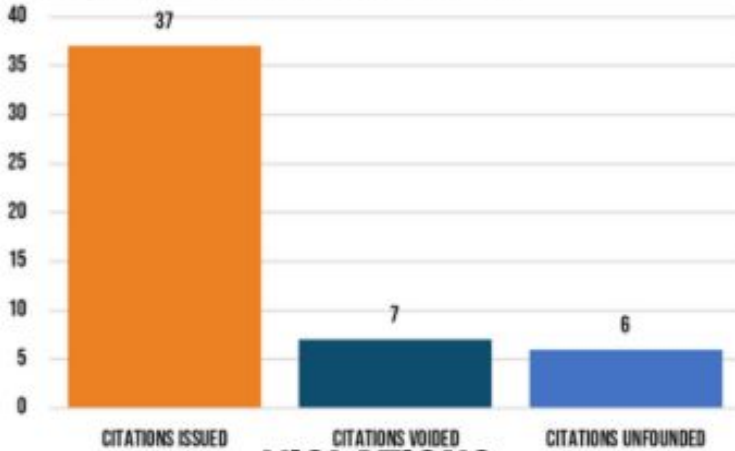

VIOLATIONS

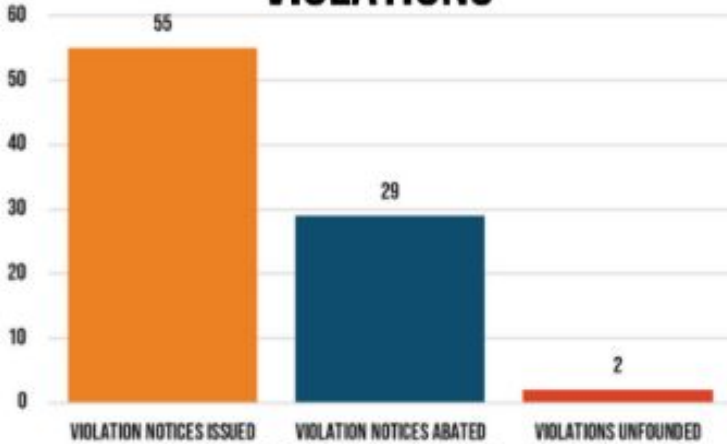


COMPLAINTS

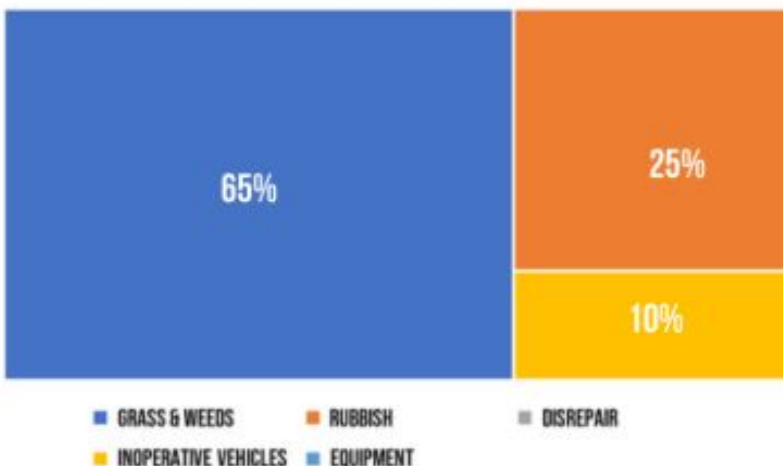


PERMITS

- **48** total permits
- **5** building only permits
- **12** zoning only permits
- **8** building & zoning permits
- **11** HVAC permits
- **12** electric permits


BUILDING ONLY

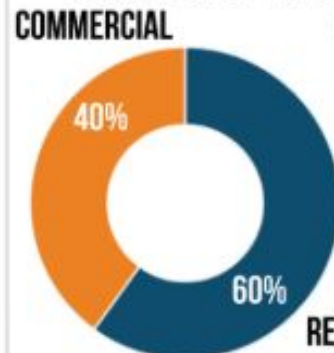


ZONING ONLY

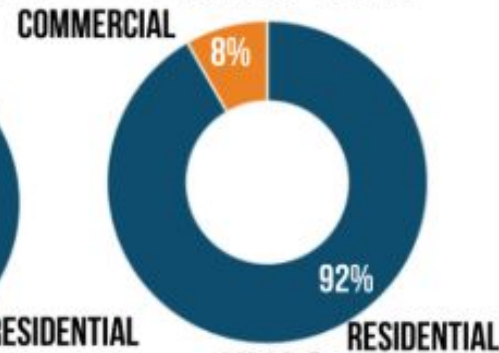

BUILDING & ZONING

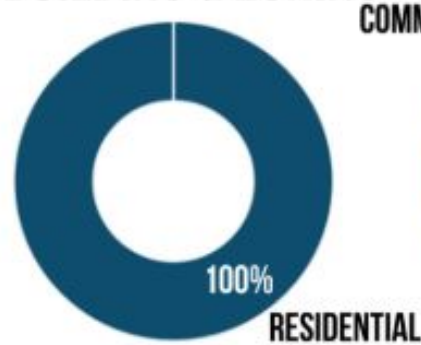

HVAC

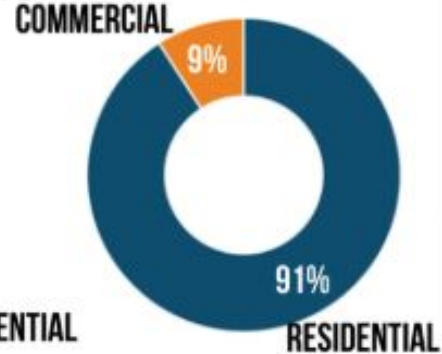

INSPECTIONS

- **97** total inspections

